


ID	Task Mode	Task Name	Duration	Start	Finish
1	✓	Project Initiation	164 days	Mon 1/1/18	Wed 6/13/18
2	✓	SOW Development	164 days	Mon 1/1/18	Wed 6/13/18
3	✓	A/E Procurement	164 days	Mon 1/1/18	Wed 6/13/18
4	✓	Procurement Complete	0 days	Wed 6/13/18	Wed 6/13/18
5	✓	Procurement Start	0 days	Mon 1/1/18	Mon 1/1/18
6	✓	Procurement	164 days	Mon 1/1/18	Wed 6/13/18
7		Design Phase	5397 days	Sat 1/1/05	Sun 11/24/19
8		Design	5342 days	Sat 1/1/05	Mon 9/30/19
9		Design Complete	0 days	Sat 1/1/05	Sat 1/1/05
10	✓	Design Start	0 days	Thu 6/14/18	Thu 6/14/18
11		Design	474 days	Thu 6/14/18	Mon 9/30/19
12		GC Procurement	55 days	Tue 10/1/19	Sun 11/24/19
13		Procurement Start	1 day	Tue 10/1/19	Tue 10/1/19
14		SOW Development to C&P	5 days	Wed 10/2/19	Sun 10/6/19
15		C&P prepares Bid Doc	13 days	Tue 10/1/19	Sun 10/13/19
16		Pre Bid Conf.	1 day	Mon 10/14/19	Mon 10/14/19
17		Bidding	30 days	Tue 10/15/19	Wed 11/13/19
18		Bids Due	1 day	Thu 11/14/19	Thu 11/14/19
19	✈	Bid Review	10 days	Fri 11/15/19	Sun 11/24/19
20	✈	Construction (All Phases)	952 days	Mon 11/25/19	Sun 7/3/22
21		Construction	857 days	Mon 11/25/19	Wed 3/30/22
22		NTP	1 day	Mon 11/25/19	Mon 11/25/19
23		Pre- Construction- Site Office Drawing Prep	60 days	Tue 11/26/19	Fri 1/24/20
24		Submit Site Office Phase 1 permit	60 days	Sat 1/25/20	Tue 3/24/20
25		Submit Site Office Phase 2 permit	90 days	Sat 1/25/20	Thu 4/23/20
26		Phase 1 Construction	99 days	Wed 3/25/20	Wed 7/1/20
27		Phase 1 Construction Substantial Complete	1 day	Thu 7/2/20	Thu 7/2/20
28	✈	Phase 1 COO/ Relocation of Terminal	394 days	Fri 7/3/20	Sat 7/31/21
29	✈	Phase 1 COO Submitted for approval	14 days	Fri 7/3/20	Thu 7/16/20
30		5th Street Terminal relocated to W street	10 days	Fri 7/17/20	Sun 7/26/20
31		5th Street Terminal Construction	330 days	Mon 7/27/20	Mon 6/21/21
32		Terminal Relocated back to 5th Street	10 days	Tue 6/22/21	Thu 7/1/21
33	✈	Removal of Temp Site office	30 days	Fri 7/2/21	Sat 7/31/21
34		Phase 2 Construction	656 days	Fri 4/24/20	Tue 2/8/22
35		Phase 2 Substantial Completion	1 day	Wed 2/9/22	Wed 2/9/22
36	✈	Phase 2 COO	20 days	Wed 2/9/22	Mon 2/28/22
37	✈	Phase 2 COO	10 days	Wed 2/9/22	Fri 2/18/22
38		Moving- New York Ave.	5 days	Sat 2/19/22	Wed 2/23/22
39		Moving- Adams Place	5 days	Thu 2/24/22	Mon 2/28/22
40		Closeout	30 days	Tue 3/1/22	Wed 3/30/22
41		Closeout	30 days	Tue 3/1/22	Wed 3/30/22
42		Project Complete	1 day	Wed 3/30/22	Wed 3/30/22

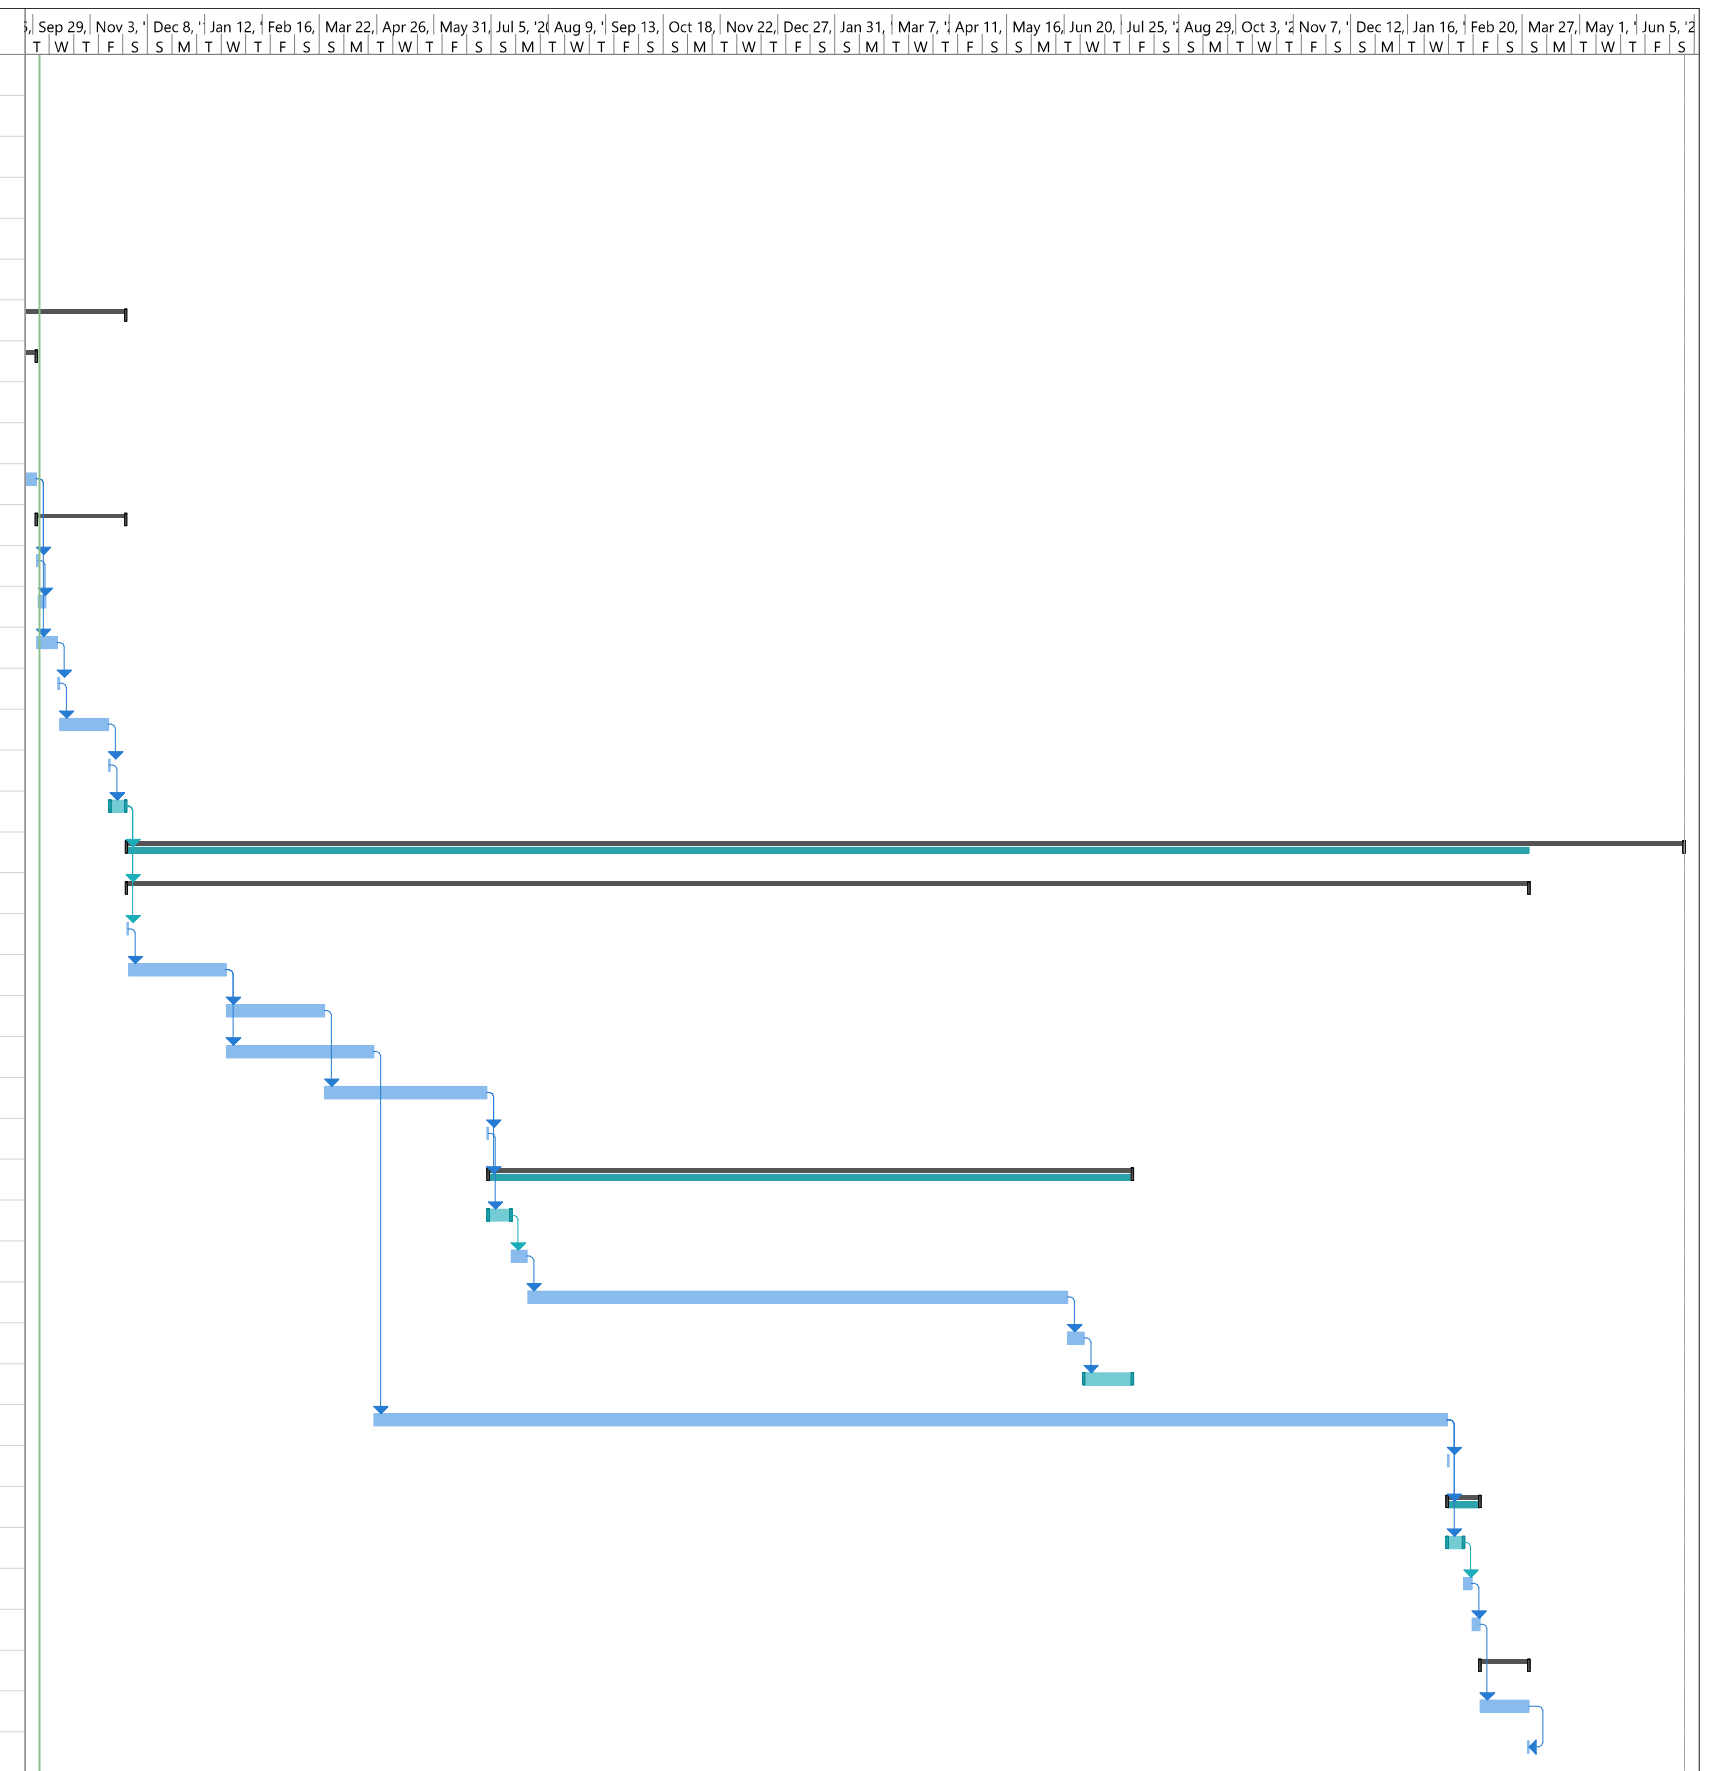

Project: 2115 5th Street NE OSS
Date: Thu 10/3/19

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			
