

EDGEWOOD REC CENTER

CONSTRUCTION UPDATE: MAY 2019

PROJECT KICKOFF

Nov 18, 2015

DESIGN AND OUTREACH

Dec 2015 - July 2017

DRAWING COMPLETION / HIRING OF CONTRACTOR

July 2017 - Dec 2018

CONSTRUCTION BEGINS

June 2018

ESTIMATED PROJECT COMPLETION

Late Summer 2019

PROJECT OVERVIEW

The Edgewood project includes replacement of the existing facility with a new, state-of-the-art recreation center containing an indoor gymnasium, fitness room, multipurpose rooms, computer, youth and senior lounges and rooftop farm. Exterior improvements include new sport courts, new playground, walking track, splash pad and athletic field improvements.

WHAT HAPPENED IN MAY:


- Continued installation of playground site walls and applied waterproofing membrane.
- Continued pouring of the splash creek walls.
- Completed hanging first floor duct.
- Began setting glass/glazing onto facility.
- Completed wall close-ins on the second floor.
- Completed framing of gym floor storage closets.
- Set ceiling sound absorption panels in the gym.
- Tied domestic and fire service utilities into public water main.
- Milled both the exterior basketball and tennis courts.

WHAT TO EXPECT IN JUNE:

- Complete all exterior glazing (glass installation).
- Complete pouring of remaining exterior site walls.
- Pour the sidewalks within the property.
- Begin setting exterior facility wall panels.
- Begin installation of site fencing.
- Begin installation of the playground equipment foundations.

PHOTO OF THE MONTH (RIGHT)

Facade glazing, taken May 30th. Window installation (glazing) began last month, including this section of the new facility that serves as a beacon to the community. These beautiful glass panels run from the lobby floor to the second floor ceiling throughout the stairwell, framing views of Trinity Washington University and beyond.

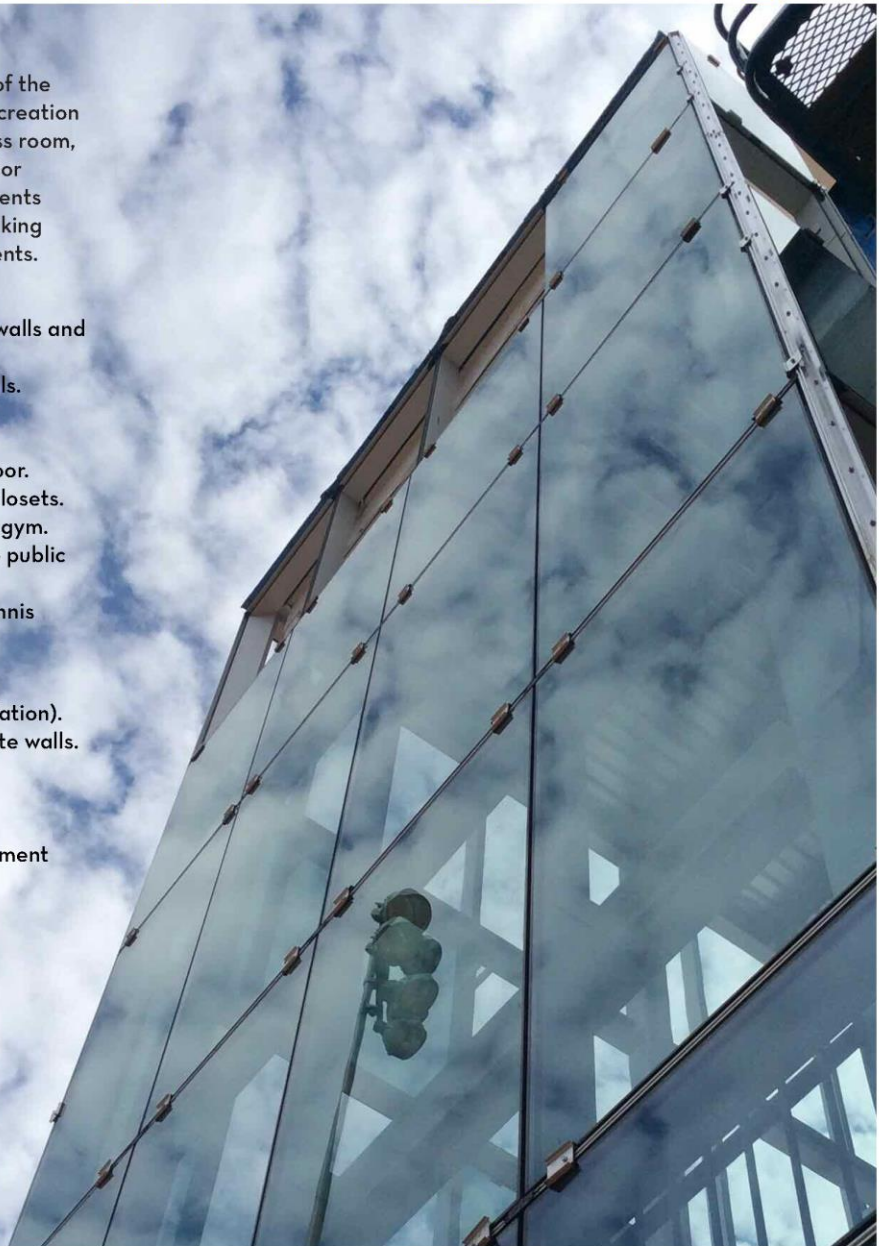

FOR ADDITIONAL INFORMATION

visit www.dgs.dc.gov/page/edgewood-recreation-center

